


Sighthill TRA

Programme summary

Revision K - July 2018

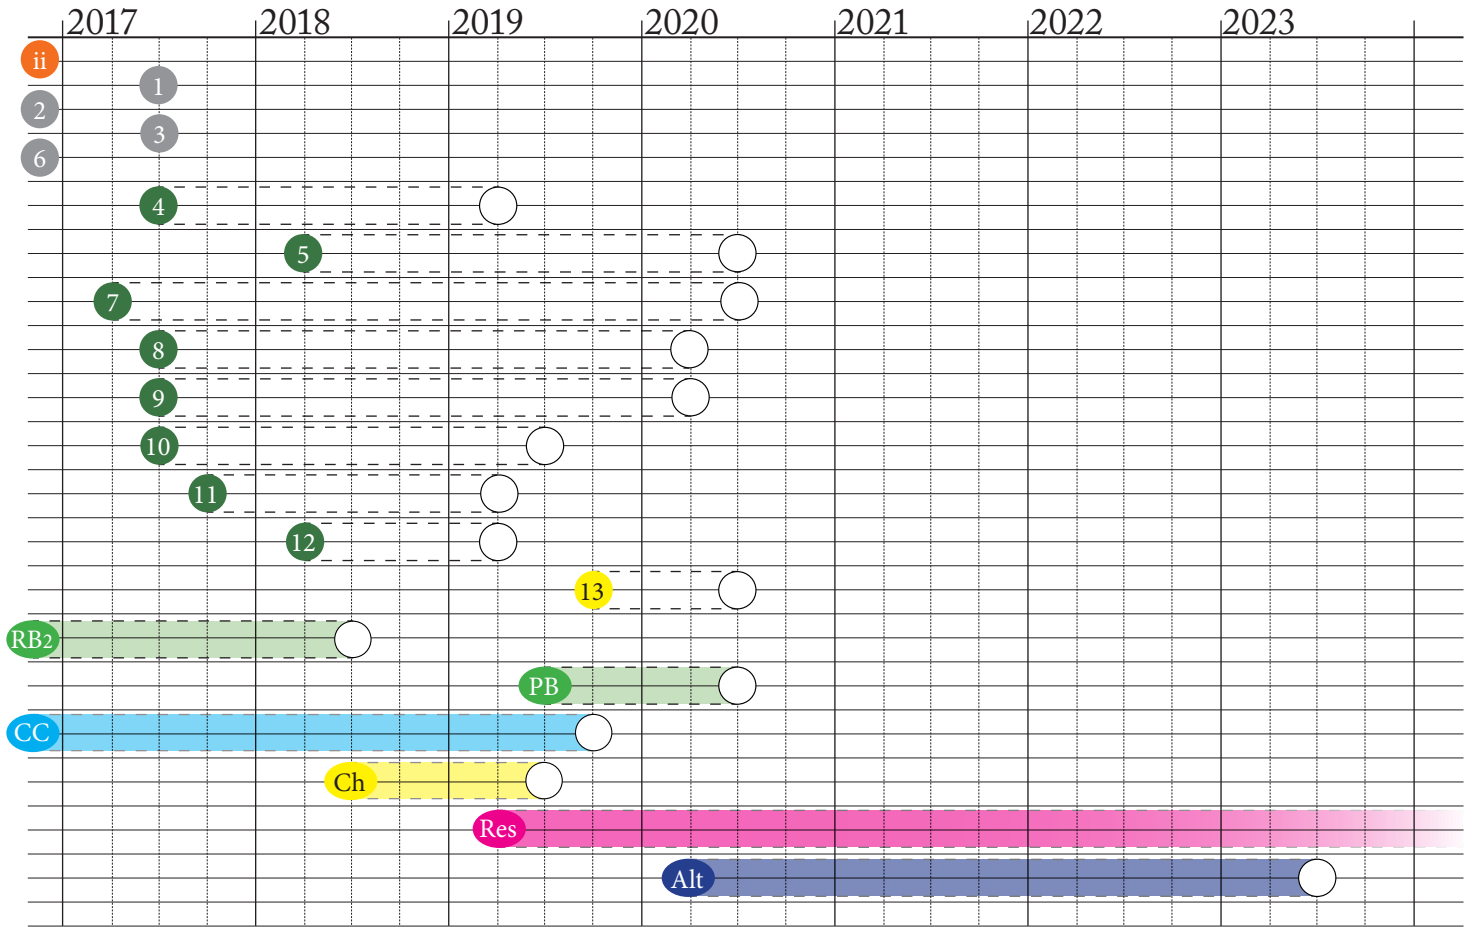

Infrastructure works:

Early 2016 - Mid 2020

- 4 Platform handover- Alternative Mid 2017 - Early 2019
 - 5 Platform handover- Residential Early 2018 - Mid 2020
 - 7 Contract 2 - Site Wide Infrastructure Early 2017 - Mid 2020
- KEY HEADLINE WORKS ACROSS THE INFRASTRUCTURE WORKS CONTRACTS
- 8 Roads Construction Mid 2017 - Early 2020
 - 9 Civic Spine Mid 2017 - Early 2020
 - 10 Earthworks Mid 2017 - Mid 2019
 - 11 Drainage Late 2017 - Early 2019
 - 12 Park / SUDS + Landscape Early 2018 - Early 2019
 - 13 Contract 4 - St Stephens Demolition + Remediation Late 2019 - Mid 2020
 - RB2 Road Bridge - New 'Black' bridge Mid 2017 - Mid 2018
 - PB Pedestrian bridge over M8 Mid 2019 - Mid 2020

Development Components:

- CC Community Campus Mid 2017 - Late 2019
- Ch St Rollox Church Mid 2018 - Mid 2019
- Res Residential developments Early 2019 - Mid 2027
- Alt Alternative development site Early 2020 - Mid 2023

Works Completed to date:

Early 2014 - Mid 2018

- i GHA - New Build Early 2014 - Late 2015
- ii GHA Demolition (Block 32/34 + 31/35) Late 2015 - Late 2016
- 1 Contract 1 - Remediation Early 2016 - Mid 2017
- 2 Contract 3 - Buchanan St Tunnel Early 2016 - Late 2016
- 3 Platform - Community campus Early 2016 - Mid 2017
- 6 Tree Felling Early 2016 - Late 2017
- RB1 Road Bridge - Service Diversion Early 2016 - Late 2016

Notes:
All programme dates provided are indicative and will be subject to change as the project progresses.
